



### BLDC WATER-WASTEWATER MASTER PROGRAM SCHEDULE

Activity ID	Activity Name	Duration	Remaining Duration	Start	Finish	Total Float	2020												2021											
							March	April	May	June	July	A	S	O	N	D	J	F	March	April	May	June								
<b>Bermuda PSG Master Schedule by WBS May 2020</b>																														
<b>Bermuda PSG Master Schedule by WBS May 2020</b>																														
<b>Master Planning</b>																														
A2960	Preliminary Program Research & Planning	15	0	03-Feb-20 A	21-Feb-20 A																									
A1000	Program Management Planning	5	0	17-Feb-20 A	06-Mar-20 A																									
A1130	Conceptual Design Review - All Priority Projects	5	0	24-Feb-20 A	06-Mar-20 A																									
A2980	Contractor Pre-Qualification	20	0	25-Feb-20 A	19-May-20 A																									
A1140	Financial Projections, Budget & Cost Tracking	5	0	02-Mar-20 A	06-Mar-20 A																									
A1170	Quantity Surveyor RFQ & Selection	25	10	07-Apr-20 A	02-Jun-20	7	Quantity Surveyor RFQ & Selection																							
<b>Tender Pkg # 1 - Stokes Point Water Crossing - Piping &amp; Pumping</b>																														
A1190	Tender Pkg # 1- Schematic Design	15	0	10-Feb-20 A	10-Apr-20 A																									
A2850	Tender Pkg # 1 - Surveying - Land Survey	10	0	10-Feb-20 A	10-Apr-20 A																									
A2880	Tender Pkg # 1 - Protected Species	1	0	10-Feb-20 A	10-Apr-20 A																									
A2890	Tender Pkg # 1 - Trench Feasibility	1	0	10-Feb-20 A	10-Apr-20 A																									
A1810	Tender Pkg # 1- Surveying - Investigation of Existing Conditions	5	0	17-Feb-20 A	21-Feb-20 A																									
A2900	Tender Pkg # 1 - Report & Recommendation	2	0	24-Feb-20 A	10-Apr-20 A																									
A2860	Tender Pkg # 1 - Surveying - Rock Bed & Sediment Depth Profile	5	0	02-Mar-20 A	06-Mar-20 A																									
A2870	Tender Pkg # 1 - Bottom Conditions & Obstructions	3	0	02-Mar-20 A	06-Mar-20 A																									
A2910	Tender Pkg # 1 - Construction Environmental Impact Remediation & Management Plan	1	0	02-Mar-20 A	01-May-20 A																									
A1770	Tender Pkg # 1 - Private Property Easement	40	20	03-Mar-20 A	16-Jun-20	61	Tender Pkg # 1 - Private Property Easement																							
A1320	Tender Pkg # 1 - Schematic Design Review	5	0	10-Apr-20 A	17-Apr-20 A																									
A1650	Tender Pkg # 1- 90% Design Submittal	10	0	17-Apr-20 A	01-May-20 A																									
A1660	Tender Pkg # 1 - 90% Design Stakeholder Review	5	0	01-May-20 A	12-May-20 A																									
A1680	Tender Pkg # 1- Planning Application & Approval	15	14	19-May-20 A	15-Jun-20	62	Tender Pkg # 1- Planning Application & Approval																							
A1690	Tender Pkg # 1 - Building Permit Application & Approval	15	14	19-May-20 A	15-Jun-20	62	Tender Pkg # 1 - Building Permit Application & Approval																							
A2920	Tender Pkg # 1 - Environmental Permit Application & Approval	20	19	19-May-20 A	15-Jun-20	62	Tender Pkg # 1 - Environmental Permit Application & Approval																							
A1670	Tender Pkg # 1 - Engineering Design Drawings for Building Permit & Construction	5	5	19-May-20 A	26-May-20	36	Tender Pkg # 1 - Engineering Design Drawings for Building Permit & Construction																							
A1700	Tender Pkg # 1 - Quantity Surveying Estimation	5	5	03-Jun-20	09-Jun-20	31	Tender Pkg # 1 - Quantity Surveying Estimation																							
A1710	Tender Pkg # 1 - Tendering & Negotiation	10	10	10-Jun-20	23-Jun-20	31	Tender Pkg # 1 - Tendering & Negotiation																							
A1720	Tender Pkg # 1 - Tender Award & Construction Commencement	5	5	24-Jun-20	30-Jun-20	31	Tender Pkg # 1 - Tender Award & Construction Commencement																							
A2820	Tender Pkg # 1 - Submittals	5	5	01-Jul-20	08-Jul-20	31	Tender Pkg # 1 - Submittals																							
A1730	Tender Pkg # 1 - Construction	30	30	09-Jul-20	19-Aug-20	46	Tender Pkg # 1 - Construction																							
A2830	Tender Pkg # 1 - Long Lead Materials / Equipment	40	40	09-Jul-20	02-Sep-20	31	Tender Pkg # 1 - Long Lead Materials / Equipment																							
A2840	Tender Pkg # 1 - Customs Clearance	5	5	03-Sep-20	10-Sep-20	31	Tender Pkg # 1 - Customs Clearance																							
A1760	Tender Pkg # 1 - Install Long Lead Materials	10	10	11-Sep-20	24-Sep-20	31	Tender Pkg # 1 - Install Long Lead Materials																							
A2490	Tender Pkg # 1- Commissioning	5	5	25-Sep-20	01-Oct-20	31	Tender Pkg # 1- Commissioning																							
A1740	Tender Pkg # 1 - Demobilization	5	5	02-Oct-20	08-Oct-20	157	Tender Pkg # 1 - Demobilization																							
A1750	Tender Pkg # 1 - As Builts	30	30	09-Oct-20	20-Nov-20	157	Tender Pkg # 1 - As Builts																							
<b>Tender Pkg # 2A - Stokes Point to St. Echo Lane - Piping &amp; Pumping Systems</b>																														
A1160	Tender Pkg # 2A - Schematic Design	5	0	25-Feb-20 A	27-Mar-20 A																									


█ Remaining Level of Effort      Primary Baseline      Remaining Work  
 Actual Level of Effort      Actual Work      Critical Remaining Work

Date	Revision	Checked	Approved
19-May-20	Bi-Monthly Update	JM	





### BLDC WATER-WASTEWATER MASTER PROGRAM SCHEDULE

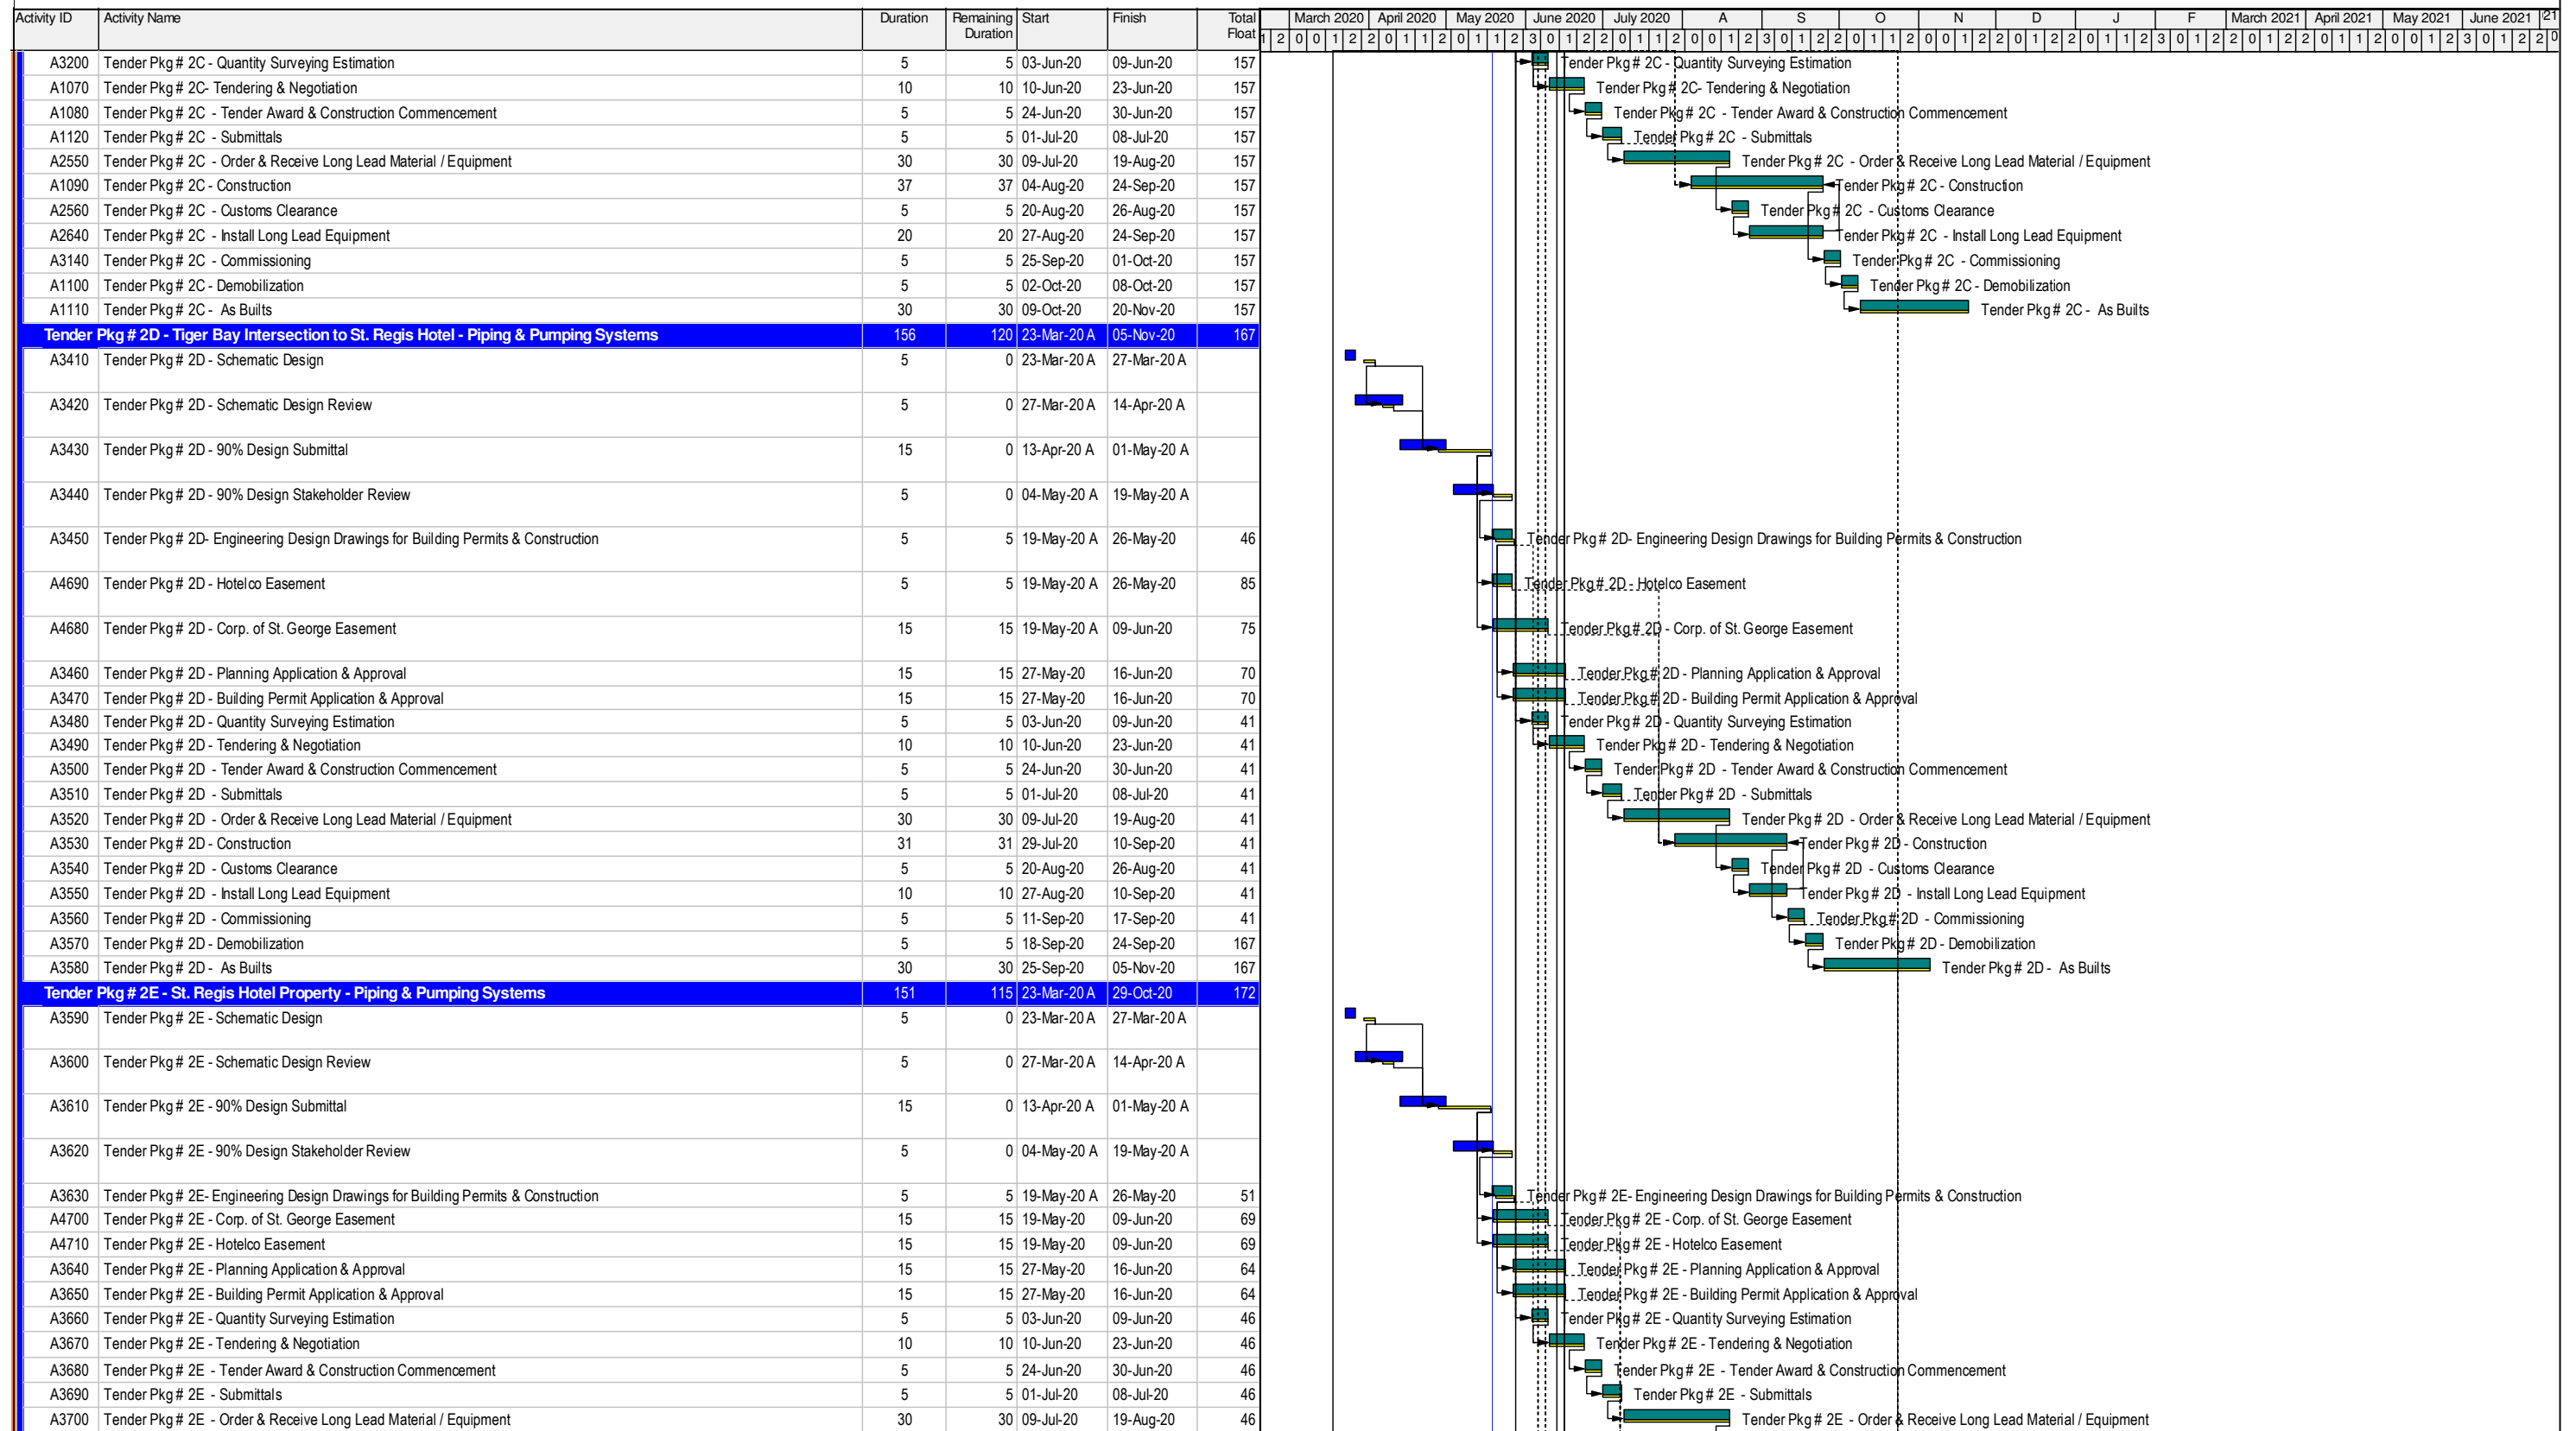

█ Remaining Level of Effort     █ Primary Baseline     █ Remaining Work  
█ Actual Level of Effort     █ Actual Work     █ Critical Remaining Work



Date	Revision	Checked	Approved
19-May-20	Bi-Monthly Update	JM	







### BLDC WATER-WASTEWATER MASTER PROGRAM SCHEDULE

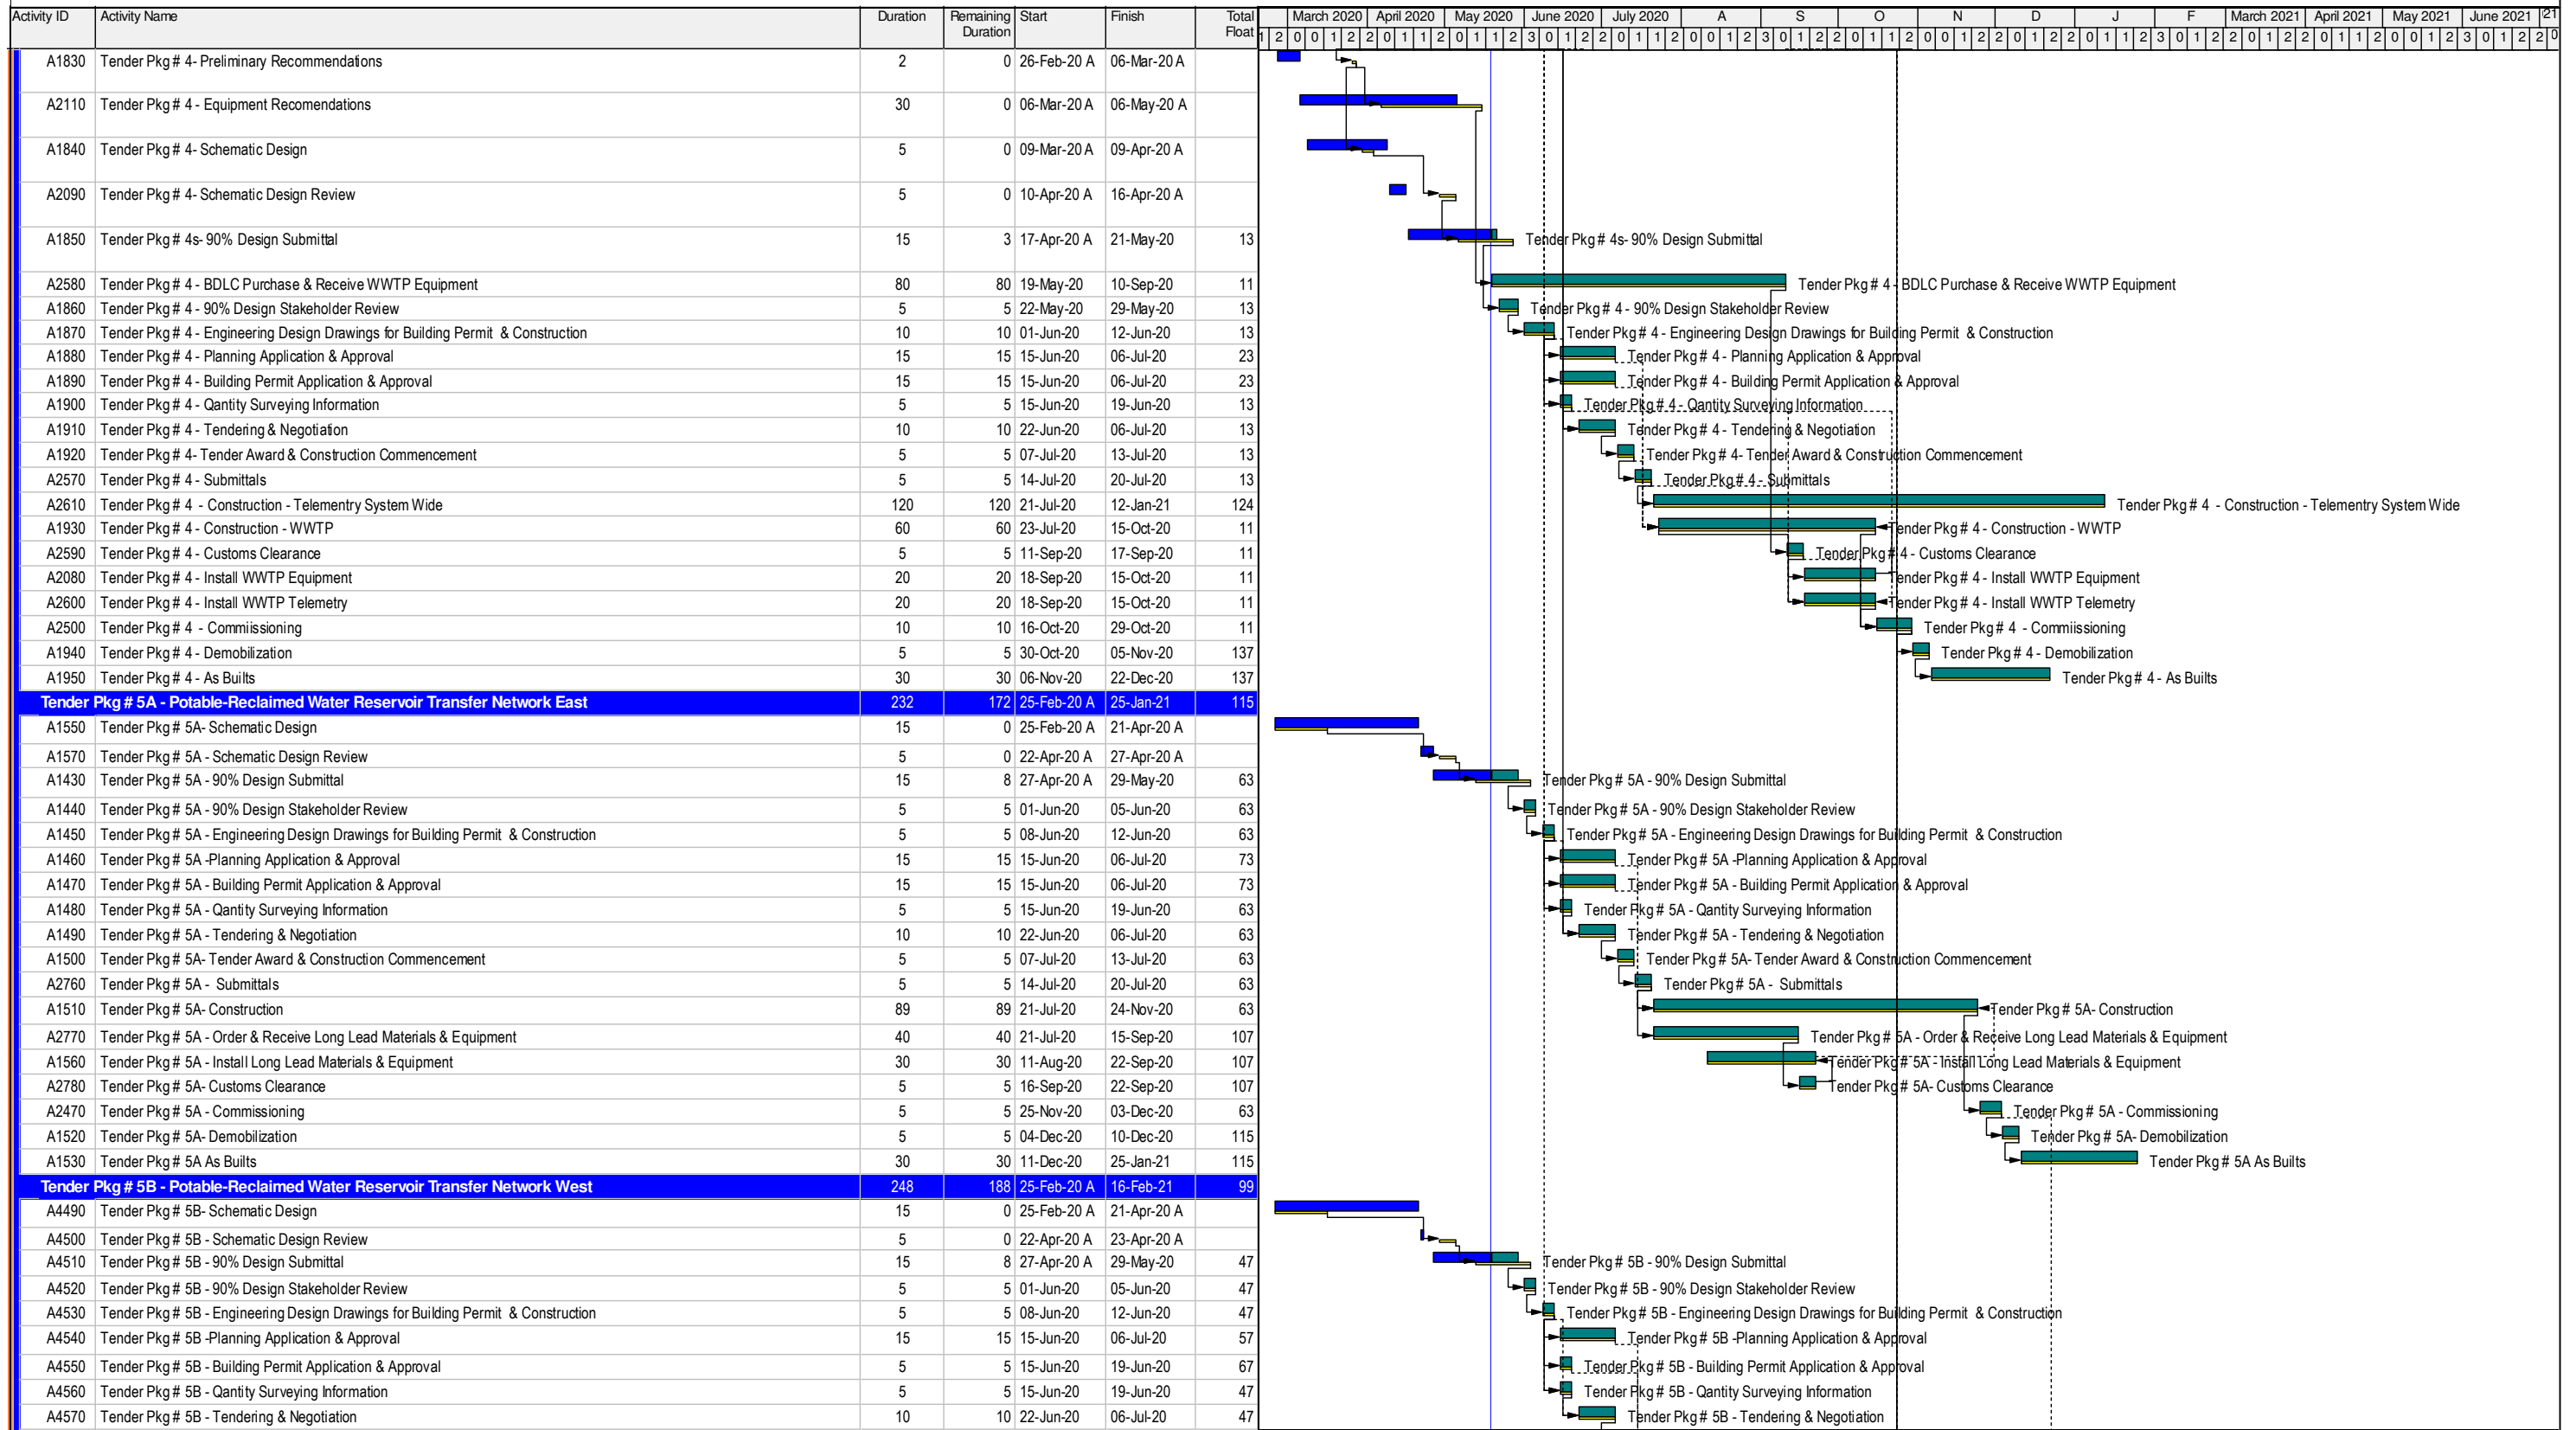


Date	Revision	Checked	Approved
19-May-20	Bi-Monthly Update	JM	



## BLDC WATER-WASTEWATER MASTER PROGRAM SCHEDULE

Activity ID	Activity Name	Duration	Remaining Duration	Start	Finish	Total Float	March 2020	April 2020	May 2020	June 2020	July 2020	A	S	O	N	D	J	F	March 2021	April 2021	May 2021	June 2021
A4580	Tender Pkg # 5B- Tender Award & Construction Commencement	5	5	07-Jul-20	13-Jul-20	47																
A4590	Tender Pkg # 5B - Submittals	5	5	14-Jul-20	20-Jul-20	47																
A4600	Tender Pkg # 5B- Construction	105	105	21-Jul-20	18-Dec-20	47																
A4610	Tender Pkg # 5B - Order & Receive Long Lead Materials & Equipment	40	40	21-Jul-20	15-Sep-20	47																
A4620	Tender Pkg # 5B- Customs Clearance	5	5	16-Sep-20	22-Sep-20	47																
A4630	Tender Pkg # 5B - Install Long Lead Materials & Equipment	60	60	23-Sep-20	18-Dec-20	47																
A4640	Tender Pkg # 5B - Commissioning	5	5	21-Dec-20	28-Dec-20	47																
A4650	Tender Pkg # 5B- Demobilization	5	5	29-Dec-20	05-Jan-21	99																
A4660	Tender Pkg # 5B As Builts	30	30	06-Jan-21	16-Feb-21	99																
<b>Final Connections at Hotel</b>																						
A2930	Final Sanitary Sewer Connections at Hotel	20	20	30-Oct-20	01-Dec-20	11																
A2940	Commissioning of Sanitary Sewer Connection at Hotel	5	5	02-Dec-20	08-Dec-20	11																
A2950	Final Acceptance of Sanitary Sewer Connection at Hotel	5	5	09-Dec-20	15-Dec-20	11																
A2990	Project Complete- Sanitary Sewer Connection	0	0		15-Dec-20*	11																
A3000	Final Recalimed Water Connection at Hotel	10	10	29-Dec-20	12-Jan-21	47																
A3210	Commissioning of Reclaimed Water Connection at Hotel	5	5	13-Jan-21	19-Jan-21	47																
A3820	Final Acceptance - Reclaimed Water Connection at Hotel	5	5	20-Jan-21	26-Jan-21	47																
A3830	Project Complete - Reclaimed Water Connection	0	0		26-Jan-21*	47																

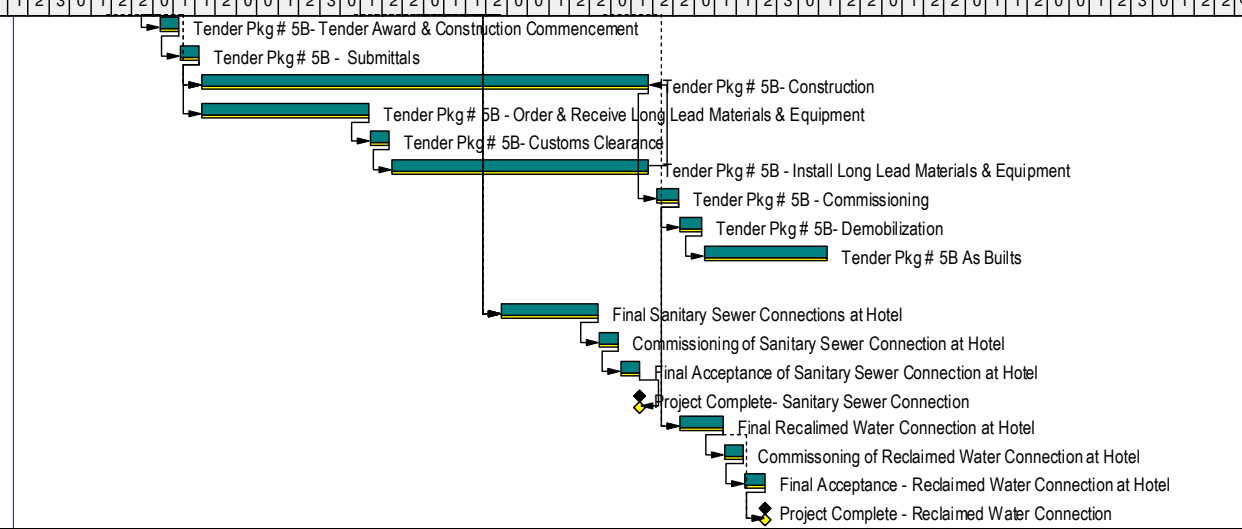

Remaining Level of Effort	Primary Baseline	Remaining Work
Actual Level of Effort	Actual Work	Critical Remaining Work

Date	Revision	Checked	Approved
19-May-20	Bi-Monthly Update	JM	
